First & Final

SBR No. 31/14-15

DATED 26-12-14

T/C-001-13-000052

M. A. R. 57 (Rule 116)

Measurement Book

No. B 310307

Serial No. ..... CE/EE(S)/42/WO/03/14-15 Dt 11/12/14.

Name of Work ... Shifting of high mast From Tubular poles To from IAP Road to Yelahanka Constituency Ward 16 & 4

Name of Contractor or nature of Agency ..... M/s Sri Lakshmi Narasimha Electricals

Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	1c Supplying of lighting Emmitting Diode (LED) Street Light fittings fabricated with die cast aluminum base with suitable heat Sink for heat dissipation, the fitting should comprise efficient electronic driver & LED's (with 100-120 Lumens/LED) completely wired to operate on 230V 50Hz AC supply (Certificate for driver performance & LED lumens output CM 80 should be furnished) (cree/nichia/Osram make optically designed high efficiency LED lights should be used polycarbonate transparent cover with IP-66 protection (INCLUDING) (50000 Burning Hours) (Allow ML-24] II Group B A) 20 watts						
					9 Nos	5,800.00	52,200.00

M. A. R. 57 (Rule 116)
Measurement Book

No. B 310311

Serial No. .....
Name of Work ..... From..... To.....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Casting & suitable foundation for the Octogonal Pole including designing and cost of all materials like Anchor Plates, Template and Washers labour charges, all other incidental charges etc, complete as per specification.				2 Nos	4929.74	103524.54
	Hire charges components for Tractor 50 HP, Sl No 20 Page No XXXIV. KPWD SR Civil 2010-11				2days	2240.00	4480.00
	Hire charges Components for Crane charges Sl No 66 Page No XXXVI, KPWD SR CIVIL 2011-12				3days	3200.00	9,600.00

E.E. (Electricals)

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
27.	Erection of suspension clamp messenger	25 to 95 sqmm bear			28 No	85.00	2,380.00
28.	Erection of Anchor clamp messenger	25 to 95 sqmm bear			2 No	85.00	170.00
29.	Installation of insulation piercing connector for main to street light Main: 16-95 sqmm Tap: 1.5-10 sqmm (EP 95)				56 No	40.00	2,240.00
						Total	4,77,434.00
	Since Quoted 9.10% below	Subtract T.P				(-)	43,446.50
						Grand Total	4,33,994.00

M. A. R. 57 (Rule 116)
Measurement Book

No. B 310313

Serial No. .....
Name of Work ..... From..... To.....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
	2	3	4	5	6	7	8
	Details of work						

LED Street lights Near Oriental English school, -AMS c/o, 6th cwc
opp # 270 to opp # 7: Below high tension line
Pillar - 1

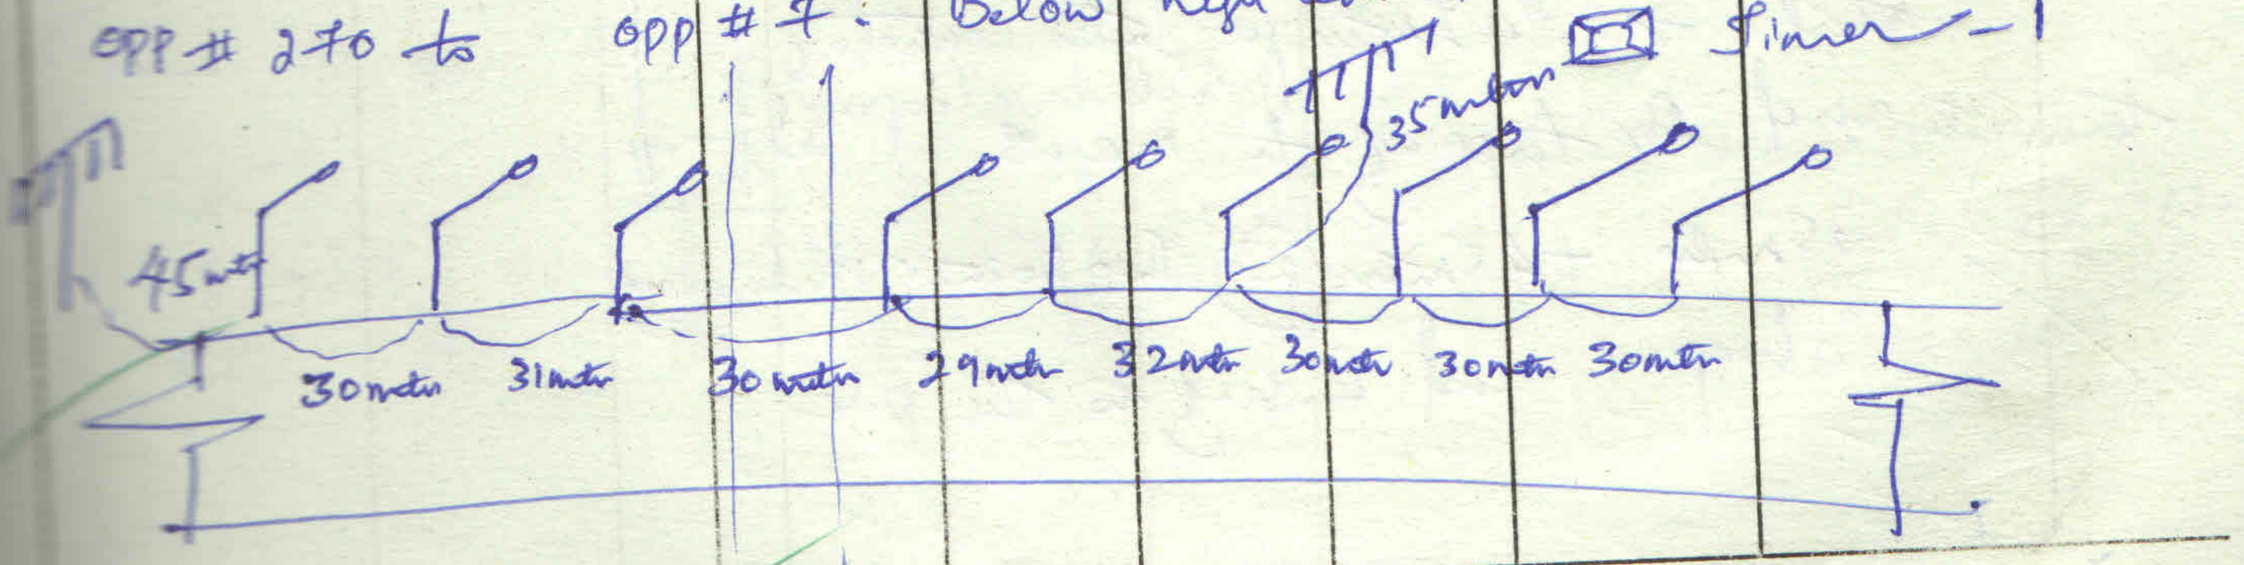

MEASUREMENT BOOK

Date 1	Full description, etc, of work 2	Dimensions Number 3	Length 4	Breadth 5	Depth 6	Contents 7	Reference to last Measurement 8
	LED Lights 24 watts → 9 Nos Long Bracket of 40mm dia — 9 Nos 4 core 16 Sqmm L-T. UG cable Total → 242 mtrs for Taker connecting including Looping & termination and for tapping to mains. 35 mtr + 45 mtr @ Two points including Looping and Raising to the pole.					Long bracket Welding Relocated pole of 5 mtr Erected.	

MEASUREMENT BOOK

EE/ELE/ / / BR No. 31/14-15

Dt. 27-12-14

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Certificate :- Work done Satisfactorily C/f to C					Bill : IT 1% VAT 4% FSD 5% LWC 1% CBF.D.1% deductions Cheque	H33986:00 H340:00 17359:00 21.699:00 H340:00 H34:00 H8,172:00 3,85,81H:00

ಲೆಕ್ಕಶೀರ್ಷಿಕೆ P-0298. m&R to Electricals

ರೂ: H33986:00 ಆಡಿಟ್ ಮಾಡಿ ಸ್ವೀಕರಿಸಿದೆ

ರೂ: 3,85,81H:00 ಚೆಕ್ ನೀಡಬಹುದಾಗಿದೆ

ರೂ: H8,172:00 ಹೊಂದಾಣಿಕೆ ಮಾಡಿದೆ

ಲೆಕ್ಕ ಅಧೀಕ್ಷಕರು

ಕಾ.ಪಾ.ಅ.(ವಿ) ಯಲಹಂಕ ವಲಯ
